



DEPARTMENT OF ENGINEERING AND PLANNING  
 Division of Engineering  
 One Spring Street  
 Newton, New Jersey 07860  
 973-579-0430  
[dpw@sussex.nj.us](mailto:dpw@sussex.nj.us)  
 John C. Risko, P.E., P.L.S., P.P.  
 Division Director/Assistant County Engineer

**Project Completion Notice – D-45 Culvert Replacement Distributed: August 30, 2013**

**Project:**

**D-45 Culvert Replacement**

CR-629 (Wykertown Road), Frankford Township

**Construction Forces:**

- Sussex County Division of Public Works
- Sussex County Office of Bridge & Traffic Safety

**Schedule:**

- Construction Start / Road Closure Date: Thursday, August 22
- Construction Completion / Road Opening Date: Friday, August 30

**Traffic Control:**

- As of Friday, August 30, CR-629 (Wykertown Road) has been reopened to traffic.
- Breakaway Barriers and Traffic Drum road closures have been removed
- Detour Sign Removal is on-going and will be completed on or about 9/3.

**Construction Activities:**

- ✓ Install / Implement road closure and detour - *Complete*
- ✓ Install Stream Protection and Sediment Control Measures - *Complete*
- ✓ Remove existing Corrugate Metal Pipe (CMP) Culvert - *Complete*
- ✓ Install new Reinforced Concrete Pipe (RCP) Culvert - *Complete*
- ✓ Regrade roadway and shoulders - *Complete*
- ✓ Repave Asphalt Roadway – *Complete*
- ✓ Reopen Roadway – *Complete*
- Remove Detour Signage – *In Progress*

**Contact Information:**


For more information about this project please feel free to contact Matt Sinke, Senior Engineer, of the Sussex County Division of Engineering at 973-579-0430 or [dpw@sussex.nj.us](mailto:dpw@sussex.nj.us)



D-45 Culvert: Stream Control Installation Upstream of Culvert



D-45 Culvert: Compacting Roadway Backfill along Replaced Culvert

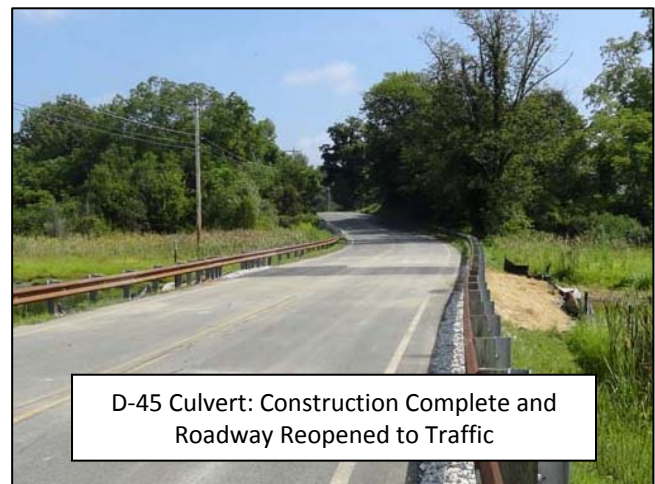

D-45 Culvert: Construction Complete and Roadway Reopened to Traffic
