



DEPARTMENT OF ENGINEERING AND PLANNING
Division of Engineering
One Spring Street
Newton, New Jersey 07860
973-579-0430
dpw@sussex.nj.us
John C. Risko, P.E., P.L.S., P.P.
Division Director/Assistant County Engineer

Project Status – Bridge E-07 (Franklin Viaduct) Distributed: May 3, 2013

Project:

Replacement of Sussex County Bridge E-07 Carrying County Route 631 (North Church Road) over Wallkill River and New York Susquehanna & Western Railroad

Designer: Cherry, Weber and Associates


Contractor: Awarded to Ritacco Construction, Inc., of Belleville, NJ for \$8,174,000.00

Schedule:

Drive sheeting, test piles & production piles. Excavate foundations. Form and pour footings/pile caps.
Construction Completion Date: December 31, 2013

Construction Activities:

- ✓ Implement road closure and detour
- ✓ Demolition of bridge superstructure and ramp
- ✓ Demolition of substructure, abutments and footings
- Installation of sheeting and piles (75%)
- Placement of reinforced concrete footings, abutments, wing walls and bridge piers (First footing poured)
- Installation of deck beams (Fabrication 75% complete)
- Construction of reinforced concrete deck (Deck pans released for fabrication)
- Construction of reinforced concrete bridge sidewalk and parapets
- Installation of bridge railing and lighting (Released)
- Placement of backfill and drainage structures (Structures ordered)
- Construction of reinforced concrete approach slabs
- Roadway paving and striping
- Installation of beam guide rail
- Topsoil, seed and landscaping

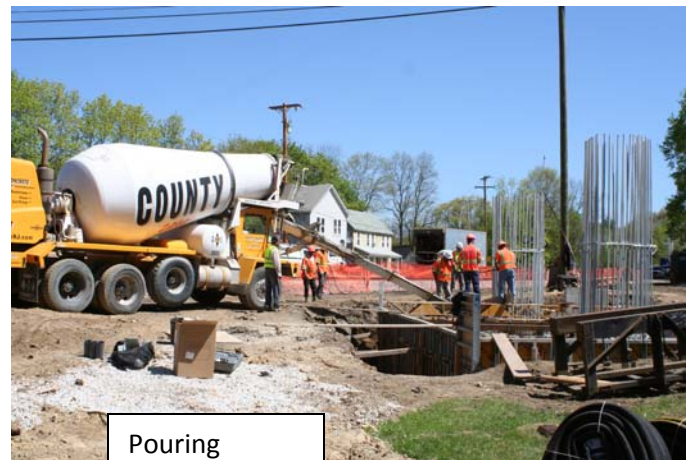

Pouring concrete at Pier 4 footing




For more information about this project please feel free to contact Charles Porter, P.E., at the Sussex County Division of Engineering at 973-579-0430 or dpw@sussex.nj.us

Future updates of the project schedule will be provided as dates and durations are confirmed.



DEPARTMENT OF ENGINEERING AND PLANNING
Division of Engineering
One Spring Street
Newton, New Jersey 07860
973-579-0430
dpw@sussex.nj.us
John C. Risko, P.E., P.L.S., P.P.
Division Director/Assistant County Engineer

Project Status – Bridge E-07 (Franklin Viaduct) Distributed: May 3, 2013

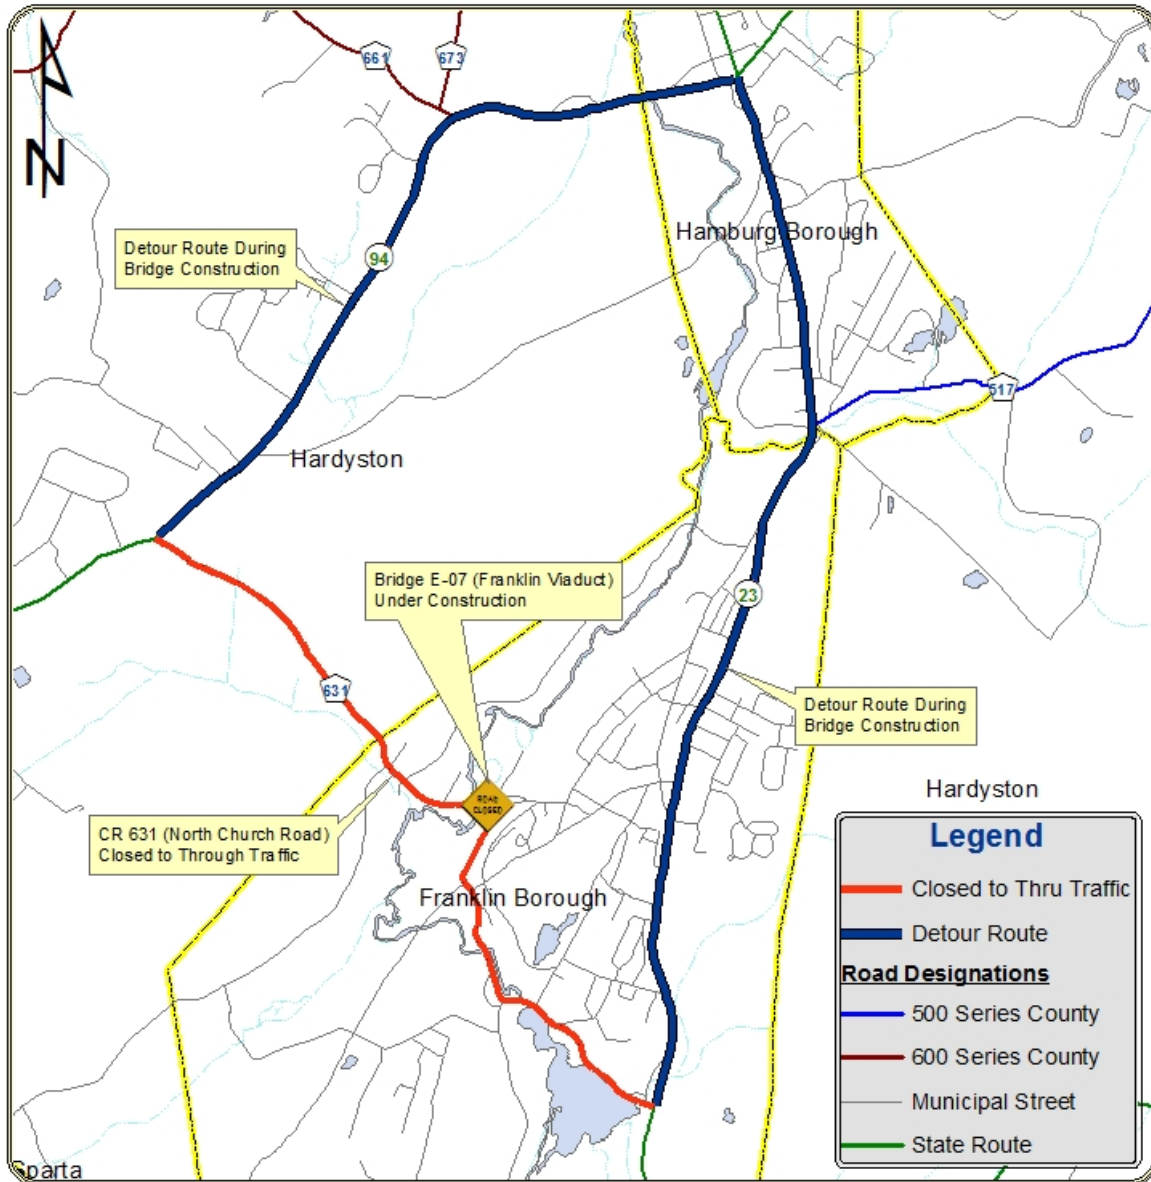

PROJECT DETOUR MAP
